

PREPARED FOR
Pat Henderson
1208 Oak Hollow Dr, Austin TX


Henderson bathroom — Daily Report

Daily report · Crew: 3 · Hours: 8 · Weather: Sunny, 88°F


WORK COMPLETED
Finished demo and hauled out the old tub surround. Subfloor is solid — no water damage. Started setting cement board on the shower walls.

PHOTOS

Shower

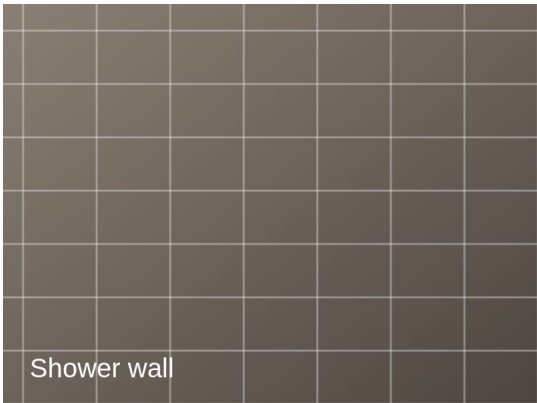


Old surround out, studs exposed




Cement board going up

Floor

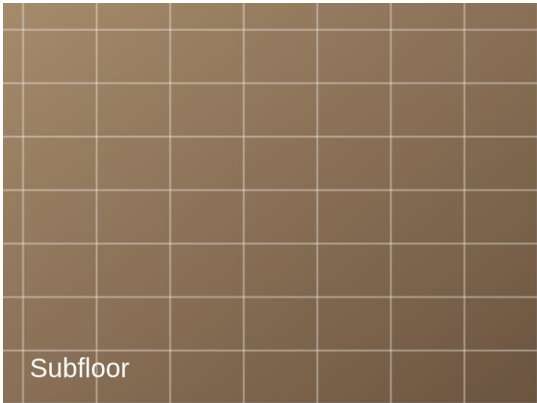

Subfloor checked — dry and solid



Debris hauled away

ISSUES

Grout color the homeowner picked is backordered about a week.

NEXT STEPS

Finish cement board and waterproofing tomorrow. Tile starts Thursday.
